

Lands known as “RB Central” at
Rockbrook, Carmanhall Road, Sandyford
Business District, Sandyford, Dublin 18
Outline Construction & Demolition Waste
Management Plan

April 2019

Document Control

Document Number: 152217-R3-PL2

Revision	Description	Date	Prepared	Checked	Approved
PL0	Outline C&D Waste Management Plan	29/03/19	E. Carr	P. Casey	D. Clarke
PL1	Planning issue	10/04/19	M. Richardson	P. Casey	D. Clarke
PL2	Planning Issue	17/4/2019	M. Richardson	P. Casey	D. Clarke

Table of Contents

Document Control	i
Table of Contents	ii
1 Introduction	1
2 Construction & Demolition Waste Management	2
2.1 Background	2
2.2 Best Practice	2
2.3 Prevention of Waste	2
2.4 Reuse of Waste	3
2.5 Recycling of Waste	3
2.6 Overall Management of Construction and Demolition Waste	3
2.7 Construction Management Plan	3
2.7.1 Disposal of Water, Wastewater and Sewage	3
2.7.2 Water Disposal	4
2.7.3 Working Hours	4
2.7.4 Waste Management Control Policy	4
2.7.5 Control of Fuels and Lubricants	4
2.7.6 Site Compound Layout	4
2.7.7 Car Parking Arrangements	5
2.7.8 Traffic Management Procedures / Generation	5
2.7.9 Air Quality	6
2.8 Noise and Vibration	6
2.8.1 Noise	6
2.8.2 Vibration	7
2.8.3 Noise and Vibration Mitigating Measures	7
2.9 Indicative On-Site Waste Construction & Demolition Waste Management Plan	9
2.9.1 Proposals for Minimisation, Reuse and Recycling of C&D Waste	9
2.9.2 Demolition Procedures	11
2.9.3 Assignment of Responsibilities	11
2.9.4 Training	11
2.9.5 Waste Auditing	11
3 Waste Management Legislation and Obligations	14
3.1 Relevant Waste Management Legislation	14
3.1.1 Waste Management (Landfill Levy) Regulations 2015, S.I. No. 189/2015	14

3.1.2	Waste Management (Facility Permit and Registration) (Amendment) Regulations 2015, S.I. No. 198/2015	14
3.1.3	Waste Management (Licensing) (Amendment) Regulations 2010, S.I. No. 350/2010	14
3.1.4	Waste Management (Collection Permit) (Amendment) Regulations 2016, S.I. No. 24/2016	14
3.1.5	Waste Management (Movement of Hazardous Waste) Regulations 1998, S.I. No. 14/1998..	14
3.1.6	Waste Management (Shipments of Waste) Regulations 2007, S.I. No. 419/2007.....	14
3.1.7	Waste Classification, List of Waste and Determining if Waste is Hazardous or Non-Hazardous, 2015	15
3.1.8	Carriage of Dangerous Goods by Road Regulations 2015, S.I. No. 288/2015.....	15
4	Preliminary Construction Traffic Management	16
4.1	Construction Traffic Access to the Site	16
4.1.1	Location and access to the site	16
4.1.2	Definition of Construction Traffic	17
4.2	Management of Construction Traffic around the Carmanhall Road Site.....	17
4.3	Proof of Compliance with Traffic Restrictions.....	18
4.4	Construction Traffic Access to site via Carmanhall Road	18
4.4.1	Traffic Management Procedures / Generation	18
4.4.2	Traffic management - Internal Site Extents.....	19
4.4.3	Traffic management coordination meetings	19
4.4.4	Construction Access Road required behaviours.....	19
4.4.5	Loading/Unloading locations	20
4.4.6	Emergency Access.....	20
4.4.7	Asset Protection	20

1 Introduction

A Main Contractor has not yet been appointed to carry out the proposed works. Once appointed, it will be the responsibility of the Main Contractor to prepare and submit a detailed construction management plan. This will be submitted to the local authority for approval by the client and used to support response to relevant planning conditions. The Construction and Demolition Waste Management Plan will be a live document that will be updated throughout the project lifecycle by the Main Contractor as required.

The site is 'Lands known as "RB Central" at Rockbrook, Carmanhall Road, Sandyford Business District, Sandyford, Dublin 18. '

The proposed development is to be constructed on sections of the building that were constructed prior to cessation of the previous site development due to the economic downturn. The previously constructed building elements consist primarily of basement and podium level construction components, including the vast majority of associated bulk excavations. The premises have a plan area of approximately 2.02 hectares in total. Please refer to Figure 1 for the location of the site.

The development will consist of 2 no. residential blocks ranging in height from 5-14 storeys comprising a total of 428 no. apartments (including all balconies, terraces and roof gardens) arranged around two courtyards; communal and public open spaces including boulevards; 4 no. ground floor retail units; resident community uses and crèche with outdoor play area. The development will also include revisions to the existing basement levels including car and bicycle parking provision with new vehicular access from Carmanhall Road; apartment storage areas; waste storage areas; ESB substation and switch room and plant/service areas. The development will also include all piped infrastructure and ducting; green roofs; changes in level; internal roads and pathways; pedestrian access points; services provision; landscaping and boundary treatments and all associated site development and excavation works above and below ground."

Access to the development will be via the existing access point from Blackthorn Drive and the new access points from Carmanhall Road. The layout of the proposed scheme is detailed in a series of planning drawings prepared by TOT Architects.

This report was prepared for Dun Laoghaire Rathdown County Council (DLRCC) in relation to the planning application for the proposed development and deals specifically with the Outline Construction and Demolition Waste Management Plan.

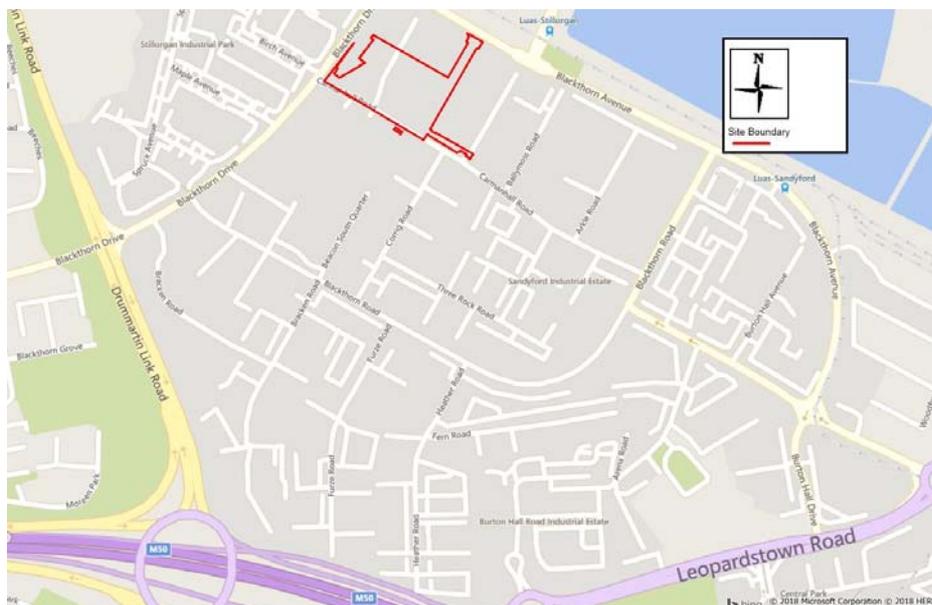


Figure 1 - Proposed Site Location and surrounding road network

2 Construction & Demolition Waste Management

2.1 Background

The purpose of the Construction and Demolition Waste Management Plan (C&D WMP) is to provide the information necessary to ensure that the management of C&D waste at the site is undertaken in accordance with current legal and industry standards including the *Waste Management Act 1996* and associated Regulations, *Litter Act 1997* and the *Eastern-Midlands Region (EMR) Waste Management Plan 2015-2021*.

This section was prepared in accordance with the 'Best Practice Guidelines on the Preparation of Waste Management Plans for Construction & Demolition Projects' for the planning application of the proposed development and outlines a Preliminary Construction & Demolition Waste Management Plan for the proposed construction works at the site.

2.2 Best Practice

The management of construction and demolition waste should reflect the waste management hierarchy, with waste prevention and minimisation being the first priority succeeded by reuse and recycling.

During site clearance and construction works, there are numerous opportunities for the beneficial reuse and recycling of the demolition materials. The subsequent use of recycled materials in construction works also reduces the quantities of waste which ultimately needs to be consigned to landfill sites.

Recycling of material will need to comply with waste management legislation.

2.3 Prevention of Waste

The primary effort therefore should be to engage in waste prevention and reduce the amount of waste generated in the first place i.e. minimise the resources needed to do the job.

Prevention is financially advantageous as it reduces the purchase of construction materials and obviates the need to remove wastes from site. It is important to emphasise the potential for certain purchasing procedures to contribute to a reduction in excessive material wastage on site.

Examples include:

- ensuring materials are ordered on an "as needed" basis to prevent over supply to site;
- purchasing construction materials in shape, dimensions and form that minimises the creation of excessive scrap waste on site;
- ensuring correct storage and handling of construction materials to minimise generation of damaged materials/waste, e.g. keeping deliveries packaged until they are ready to be used;
- ensuring correct sequencing of operations; and
- assigning individual responsibility (through appropriate contractual arrangements) to sub-contractors for the purchase of raw materials and for the management of wastes arising from their activities, thereby ensuring that available resources are not expended in an extravagant manner at the expense of the main contractor.

2.4 Reuse of Waste

Material that is generated should be reused on site or salvaged for subsequent reuse to the greatest extent possible and disposal should only be considered as a last resort. Initiatives should be put in place to maximise the efficient use/reuse of materials.

2.5 Recycling of Waste

There are a number of established markets available for the beneficial use of C&D waste:

- waste timber can be:
 - recycled as shuttering or hoarding, or
 - sent for reprocessing as medium density fibreboard;
- waste concrete can be utilised as fill material for roads or in the manufacture of new concrete when arising at source; and
- in addition, the technology for the segregation and recovery of stone, for example, is well established, readily accessible and there is a large reuse market for aggregates as fill for roads and other construction projects.

2.6 Overall Management of Construction and Demolition Waste

Waste minimisation, reuse and recycling can best be managed operationally by nominating a "Construction and Demolition Waste Manager" to take responsibility for all aspects of waste management at the different stages of the Project.

This C&D Waste Manager may well be a number of different individuals over the life-cycle of the Project, but in general is intended to be a reliable person chosen from within the Contracting Team, who is technically competent and appropriately trained, who takes the responsibility to ensure that the objectives and measures within the Project Waste Management Plan are delivered and who is assigned the requisite authority to secure achievement of this purpose.

Specifically, the function of the C&D Waste Manager will be to communicate effectively with colleagues in relation to the aims and objectives for waste management on the Project. The primary responsibility for delivery of the objectives of the Waste Management Plan will fall upon the C&D Waste Manager designated at the demolition/ construction stage. A key objective for the C&D Waste Manager should be to maintain accurate records on the quantities of waste/ surpluses arising and the real cost (including purchase) associated with waste generation and management.

The preparation, application and documentation of a Project Waste Management Plan should enable all parties - including contractors, designers and competent authorities - to learn from the systematic implementation and assessment of best practice, particularly through the recording of summary information on performance outcomes.

2.7 Construction Management Plan

2.7.1 Disposal of Water, Wastewater and Sewage

All site facilities during construction will be located entirely within the site. The facilities will include canteen, toilet block and drying room for all staff/workers. These facilities will be connected to the Local Authority sewage system with local authority approval.

2.7.2 Water Disposal

Throughout the works, all surface water (water from excavations etc.) will be controlled and managed in an appropriate way to ensure all construction and demolition waste does not have an adverse effect on local sewer networks or groundwater.

2.7.3 Working Hours

It is anticipated that construction working hours will be stipulated in the planning conditions attached to the planning grant. Any working hours outside the normal construction working hours will be agreed with Dun Laoghaire Rathdown County Council. The planning of such works will take consideration of sensitive receptors, in particular any nearby businesses.

2.7.4 Waste Management Control Policy

In general:

Regular shaped skips, will be used for the duration of the demolition/ construction works. All skips will be situated in the waste segregation area on site.

Labelled skips will be available for each of the following waste types: wood, metal, brick/ rubble, canteen waste, plasterboard, paper and cardboard, other general waste and special bins for any hazardous wastes as required.

Throughout the demolition/ construction zone, covered labelled wheelie bins will be placed at designated waste depots. These bins will be taken and used by the operatives/ sub-contractors and returned to the depots after use.

The waste segregation area banksman will co-ordinate the movement of skips to and from the demolition/ construction zone. The banksman will also co-ordinate the scheduling of the approved waste collector to transport waste to the relevant permitted/ licensed waste facility.

2.7.5 Control of Fuels and Lubricants

In order to provide fuel to the relevant items of plant on site, a certified double skinned metal fuel tank with integrated pump, delivery hose, meter, filter and locking mechanism will be situated in a secure area on the construction site. It will be situated within a bund. This tank will be certified for lifting when full.

Sand piles and emergency clean up spill kits will be readily available in the event of a fuel spill. A hazardous bin will also be available to contain any spent sand or soak pads.

New metal gerry cans with proper pouring nozzles will be used to move fuel around the site for the purposes of refuelling items of small plant on site.

Drip trays will be used under items of small plant at all times. Any waste oils etc. contained in the drip trays or the bunded area will be emptied into a waste oil drum, which will be stored within the bund.

Metal gerry cans and any other items of fuel containers will be stored in certified metal bunded cabinets. Any gas bottles will be stored in a caged area at a secure location on the site. All will be properly secured at point of work.

2.7.6 Site Compound Layout

The site and associated site compound is to be enclosed by a hoarding.

2.7.7 Car Parking Arrangements

The site benefits from the previously mentioned substantially complete basement car park. Therefore, it will be proposed that limited car parking will be allocated to contractor's staff. These will be accessed via Blackthorn Drive access. It is not anticipated that there will be significant adverse impact on the existing road network since the number of vehicles will not be significant, and flows will be opposite those for the existing residential units, and out of sync with the retail units already accessing via this access point.

To minimise congestion, a traffic management plan will need to be developed by the Contractor to ensure that construction workers access the site using alternative means of transport (i.e. public transport) to mitigate negative impacts on the local network.

2.7.8 Traffic Management Procedures / Generation

All deliveries will be booked into site at least one day before delivery. All drivers will contact the site gate man 15 minutes before arrival on site.

All construction traffic will arrive along Carmanhall Road, prior to entering the proposed development site. Refer to defined construction/demolition traffic route in Section 4.1.1 of this report. All deliveries will be off-loaded without delay by the most appropriate method and escorted off site.

The site gate man will be responsible for ensuring that there is no conflict between pedestrians and vehicles entering/ exiting the site. In addition, and as required, temporary markings will be painted on the footpath either side of the site entrance to alert pedestrians.

It is predicted that there will be workforce varying in a range of approximately 30-200 personnel on site during peak construction activity depending on phasing and construction stage. For example, initial stages of construction will be limited to specific disciplines which may not require large numbers of personnel. However, multiple trades may be active on the buildings during internal fit-out of the completed superstructure on a staggered basis as the works are progressed leading to higher numbers of personnel being present. Accounting for public transport and car sharing, there could be in the order of 20 construction vehicles arriving and departing the site every day during peak construction activity.

Peak traffic movements in and out of the site should occur outside of the AM/PM rush hour traffic. Please refer to section 2.7.3 for additional information regarding working hours.

The volume of HGV movements per day will vary according to the different stages of works, including demolition. Peak HGV movements will be associated with removal off-site of concrete walls and roof cladding elements.

Demolition Works:

For a rigid HGV hauling material from the site, it will typically take 15 mins from when the rigid arrives at the site entrance, travels to the demolition area, receives its load and leaves the site. This equates to a predicted 4 HGV's per hour.

The worst-case scenario is demolition works with an estimated average of 4 HGV's per hour predicted during peak demolition activity. It is envisaged that HGV movements will be undertaken outside of AM/ PM rush hour traffic.

2.7.9 Air Quality

There is the potential for a number of emissions to the atmosphere during the demolition stage of the project. In particular, activities may generate quantities of dust. Construction vehicles, generators etc., will also give rise to some exhaust emissions.

Vehicular movements to and from the site will make use of existing roads. It is estimated that peak construction HGV movements will be 4 HGV's per hour. Considering the existing traffic levels in the area, the likely air quality impact associated with construction traffic is not significant.

A dust minimisation plan will be formulated for the demolition and construction phase of the project, as construction activities are likely to generate dust emissions. The potential for dust to be emitted depends on the type of activity being carried out in conjunction with environmental factors including levels of rainfall, wind speeds and wind direction. The potential for impact from dust depends on the distance to potentially sensitive locations and whether the wind can carry the dust to these locations. The majority of any dust produced will be deposited close to the potential source and any impacts from dust deposition will typically be within several hundred metres of the construction area.

In order to ensure that no dust nuisance occurs, a series of measures will be implemented.

Roads shall be regularly cleaned and maintained as appropriate. Hard surface roads shall be swept to remove mud and aggregate materials from their surface. Furthermore, any road that has the potential to give rise to dust must be regularly watered, as appropriate, during dry and/or windy conditions.

Vehicles delivering material with dust potential both on and off the site shall be enclosed or covered with tarpaulin at all times to ensure no potential for dust emissions.

Public roads adjacent to the site shall be regularly inspected for cleanliness, and cleaned by road sweeping as necessary.

Material handling systems and site stockpiling of materials shall be designed and laid out to minimise exposure to wind. Water misting or sprays shall be used as required if particularly dusty activities are necessary during dry or windy periods.

At all times, the procedures put in place will be strictly monitored and assessed. In the event of dust nuisance occurring outside the site boundary, satisfactory procedures will be implemented to rectify the problem.

The dust minimisation plan shall be reviewed at regular intervals during the construction phase to ensure the effectiveness of the procedures in place and to maintain the goal of minimisation of dust through the use of best practise and procedures.

Sampling and calculation of dust is to be based on Bergerhoff standard Methodology T.A. Luft Standard (VD1 2119); the EPA refer to the TA Luft guide limit 350mg/m²/day over a 30-day monitoring period

2.8 Noise and Vibration

2.8.1 Noise

There is no published Irish guidance relating to the maximum permissible noise level that may be generated during the construction phase of a project. Local authorities normally control construction activities by imposing limits on the hours of operation and consider at their discretion noise limits.

In the absence of specific noise limits, appropriate criteria relating to permissible construction noise levels for a development of this scale will be agreed with Dun Laoghaire Rathdown County Council as part of the planning conditions and will indicate the maximum permissible noise levels at adjacent

properties during construction and any related time constraints with regard hours of operation. The majority of the construction activity is expected to occur during normal working hours.

Noise monitoring to be in accordance with the following standards:

-ISO 4866

-BRE DIGEST 403

2.8.2 Vibration

There are two varieties of criteria for vibration: those dealing with human comfort and those dealing with cosmetic or structural damage to buildings. In both instances, it is appropriate to consider the magnitude of vibration in terms of Peak Particle Velocity (PPV).

It is acknowledged that humans are particularly sensitive to vibration stimuli and that any perception of vibration may lead to concern. In the case of road traffic, vibration is perceptible at around 0.5 mm/s and may become disturbing or annoying at higher magnitudes. However, higher levels of vibration are typically tolerated for single events or events of short duration. For example, piling is typically tolerated at vibration levels up to 5mm/s. This guidance is applicable to the daytime only; it is unreasonable to expect people to be tolerant of such activities during the night.

Guidance relevant to acceptable vibration within buildings is contained in the following documents:

- British Standard BS 7385 -2:1993: Evaluation and measurement for vibration in buildings. Guide to damage levels from ground borne vibration, and;
- British Standard BS 5228-2:2009: Code of practice for noise and vibration control on construction and open sites

2.8.3 Noise and Vibration Mitigating Measures

Due to the nature of the activities undertaken on a construction site, there is naturally potential for generation of significant levels of noise. A variety of items of plant may be in use, such as pneumatic breakers, excavators, lifting equipment, dumper trucks, compressors and generators. The flow of vehicular traffic to and from a construction site is also a potential source of relatively high noise levels.

The potential for vibration at neighbouring sensitive locations during construction is typically limited to demolition works, excavation works and lorry movements on uneven road surfaces.

With regard to construction activities, reference will be made to BS 5228-1:2009: Noise control on construction and open sites, which offers detailed guidance on the control of noise and vibration from demolition and construction activities. In particular, it is proposed that various practices be adopted during construction, including:

- limiting the hours during which site activities likely to create high levels of noise or vibration are permitted;
- establishing channels of communication between the contractor/developer, Local Authority and residents;
- appointing a site representative responsible for matters relating to noise and vibration;
- monitoring typical levels of noise and vibration during critical periods and at sensitive locations;
- to mitigate the potential for vibration from lorries, all site construction vehicle access points will be kept in a good condition: without potholes, or other sharp changes in grade;

- Construction of 2.4m high hoarding.

Furthermore, it is envisaged that a variety of practicable noise control measures will be employed. These may include:

- selection of plant with low inherent potential for generation of noise and/ or vibration;
- erection of barriers as necessary around noisy processes and items such as generators heavy mechanical plant or high duty compressors;
- placing of noisy / vibratory plant as far away from sensitive properties as permitted by site constraints and the use of vibration isolated support structures where necessary.

It is recommended that vibration from construction activities be limited to the values set out in section 2.8.2. It should be noted that these limits are not absolute but provide guidance as to magnitudes of vibration that are very unlikely to cause cosmetic damage. Magnitudes of vibration slightly greater than those are normally unlikely to cause cosmetic damage, but construction work creating such magnitudes should proceed with caution. Where there is existing damage these limits may need to be reduced by up to 50%.

During the construction phase of the project there will be some minor impact on nearby properties due to noise emissions from site traffic and other activities. However, given that the construction phase of the project is temporary in nature, it is expected that the various noise sources will not be excessively intrusive. Furthermore, the application of binding noise limits and hours of operation, along with implementation of appropriate noise and vibration control measures, will ensure that noise and vibration impact is kept to a minimum.

It is recommended that appropriate dilapidation records for the site and surrounding area are documented prior to the commencement of construction/demolition activities.

2.9 Indicative On-Site Waste Construction & Demolition Waste Management Plan

In the course of the Project, it is estimated that the following quantities of construction and demolition wastes/material surpluses will arise:

C& D Waste Material	Quantity	Action
Clay and Stones (Soil, Stones & Bedrock)	7,500 t (allowance)	25% to be reused on site and 75% to be recycled
Concrete (floor slabs, tanks, walls)	1,600 t	50% of any waste concrete to be recycled 50% to be properly disposed of
Masonry	20 t	100% of any waste masonry to be recycled
Wood	5 t	100% of any waste timber to be recycled
Packaging	10 t	100% of any waste packaging to be recycled
Hazardous Materials	5 t	Not envisaged at this stage of the project*
Steelwork (beams, columns, roof trusses & water tank)	10 t	Any other waste materials will be recycled where possible or disposed of appropriately
M&E Plant	20 t	
Soft Strip furnishings, fittings, etc.	10 t	
Glazing	10 t	
Insulated panel roof sheeting	10 t	
Waste paints and oils	10 t	
TOTAL Arisings	9,210 t	

Table SF1 Estimated C&D Waste Arisings on Site from Appendix 3 of Best Practice Guidelines of Waste Management Plans for C&D Projects

These quantities are provisional only and subject to further determination during construction works.

2.9.1 Proposals for Minimisation, Reuse and Recycling of C&D Waste

Construction and demolition waste will arise on the Project mainly from the site clearance, service trenches and foundation preparation.

The following are proposals for minimisation, reuse and recycling of C&D waste:

- The Purchasing Manager shall ensure that materials are ordered so that the quantity delivered, the timing of the delivery and the storage is not conducive to the creation of unnecessary waste.
- Concrete waste will be source segregated.
- Masonry and wood will be source segregated.
- Packaging will be source segregated for recycling or return to suppliers.
- Hazardous wastes will be identified, removed and kept separate from other C&D waste materials in order to avoid further contamination.
- Other C&D waste materials will be collected in receptacles with mixed C&D waste materials, for subsequent separation and disposal at a remote facility.

It is anticipated that waste materials will have to be moved off site. It is the intention to engage specialist waste service Contractors, who will possess the requisite authorisations, for the collection and movement of waste off-site, and to bring the material to a facility which currently holds a Waste Licence/ Waste Permit/ Certificate of Registration. Accordingly, it will be necessary to arrange the following waste authorisations specifically for the Project:

Authorisation Type	Specific Need for Project (Yes/No?)	
Waste Licence	Yes <input checked="" type="checkbox"/>	No <input type="checkbox"/>
Waste Permit	Yes <input checked="" type="checkbox"/>	No <input type="checkbox"/>
Waste Collection Permit	Yes <input checked="" type="checkbox"/>	No <input type="checkbox"/>
Trans frontier Shipment Notification	Yes <input type="checkbox"/>	No <input checked="" type="checkbox"/>
Movement of Hazardous Waste Form	Yes <input type="checkbox"/>	No <input checked="" type="checkbox"/>

Table SF3 Waste Authorisations Necessary for the Scheme from Appendix 3 of Best Practice Guidelines of Waste Management Plans for C&D Projects

A list of waste collection permit holders to be employed on this project will be submitted to the local authority by the contractor in their Formal Construction and Demolition Waste Management Plan for the Construction Stage.

A list of waste collection permit sites that the waste may be recovered or disposed to on this project will be submitted to the local authority by the contractor in their Formal Construction and Demolition Waste Management Plan for the Construction Stage.

2.9.2 Demolition Procedures

The demolition works shall be undertaken in a manner which maximises the potential for recycling, including source segregating waste where appropriate. Activities shall be carried out in the following sequence:

Demolition Activity Sequence	General Description
Removal of defunct plant from existing basement and necessary bulk excavations in advance of completion of the basement structure construction	e.g. Application of H & S Procedures
Storage of classified waste streams to appropriate containers prior to transport/disposal.	e.g. Secure skip containers to store waste arisings
Demolition associated with existing building interior consisting of demolition to facilitate new rising structure (i.e. cores and columns).	e.g. Application of H & S Procedures, Separation into Designated Material Fractions
Construction Activity Generated Waste	e.g. formwork, temporary hoardings or structures, waste materials arising from site activities
Source Segregation of Material Fractions	Separation into Designated Material Fractions
Transport of Material from Site to Treatment Facilities	e.g. C/D Waste Recycling Facility
Transport of Material from Site to Controlled Disposal Sites	e.g. Inertised Hazardous Landfill Site
Development Completion	e.g. Building façade and interior spaces, hard and soft landscaping, plant and green roof construction.

2.9.3 Assignment of Responsibilities

A foreman shall be designated as the Responsible Person and have overall responsibility for the implementation of the on-site Waste Management Plan.

The Responsible Person will be assigned the authority to instruct all site personnel to comply with the specific provisions of the Plan.

At the operational level, a Ganger from the main contractor and appropriate personnel from each sub-contractor on the site shall be assigned the direct responsibility to ensure that the discrete operations stated in the Waste Management Plan are performed on an on-going basis.

2.9.4 Training

Copies of the Waste Management Plan will be made available to all personnel on site. All site personnel and sub-contractors will be instructed about the objectives of the Waste Management Plan and informed of the responsibilities which fall upon them as a consequence of its provisions.

Where source segregation, selective demolition and material reuse techniques apply, each member of staff will be given instructions on how to comply with the Waste Management Plan.

Posters will be designed to reinforce the key messages within the Waste Management Plan and will be displayed prominently for the benefit of site staff.

2.9.5 Waste Auditing

The C&D Waste Manager shall arrange for full details of all arisings, movements and treatment of construction and demolition waste discards to be recorded during the construction stage of the Project.

Each consignment of C&D waste taken from the site will be subject to documentation, which will conform to Table SF4 and ensure full traceability of the material to its final destination.

Detail	Particulars
Name of Project of Origin	e.g. New Harbour Motorway
Material being Transported	e.g. Soil, Demolition Concrete, Crushed Asphalt etc.
Quantity of Material	e.g. 20.50 tonnes
Date of Material Movement	e.g. 01/07/2018
Name of Carrier	e.g. Authorised Carriers Ltd.
Destination of Material	e.g. RB Central, Sandyford Business District
Proposed Use	e.g. Use as Hardcore in Dwelling Floors

Table 1 Table SF4 Details to be Included within Transportation Dockets from Appendix 3 of Best Practice Guidelines of Waste Management Plans for C&D Projects

Details of the inputs of materials to the Construction site and the outputs of wastage arising from the Project will be investigated and recorded in a Waste Audit, which will identify the amount, nature and composition of the waste generated on the site.

The Waste Audit will examine the manner in which the waste is produced and will provide a commentary highlighting how management policies and practices may inherently contribute to the production of construction and demolition waste.

The measured waste quantities will be used to quantify the costs of management and disposal in a Waste Audit Report, which will also record lessons learned from these experiences which can be applied to future projects.

The total cost of C&D Waste management will be measured and will take account of the purchase cost of materials (including imported soil), handling costs, storage costs, transportation costs, revenue from sales, disposal costs etc. Costs will be calculated for the management of a range of C&D Waste materials, using the format shown in Table SF5.

The Table SF5 below will be completed and submitted to the Council in full following the appointment of a contractor for the works.

Material	Estimated Quantities & Costs (tonnes & Euro)
<u>SOIL</u>	
Quantity of Waste Soil(tonnes)	
Purchase Cost i.e. Import Costs (€)	
Materials Handling Costs (€)	
Material Storage Costs (€)	
Material Transportation Costs (€)	
Revenue from Material Sales (€)	
Material Disposal Costs (€)	
Material Treatment Costs (€)	
<i>Total Waste Soil Management Costs (€)</i>	
<i>Unit Waste Soil Management Costs (€)</i>	

Table SF5 Standard Record Form for Costs of C & D Waste Management from Appendix 3 of Best Practice Guidelines of Waste Management Plans for C&D Projects

Details of the quantities and types of C&D Waste arising from the Project will be forwarded to Environmental Protection Agency, local competent authority, NCDWC etc.

3 Waste Management Legislation and Obligations

3.1 Relevant Waste Management Legislation

This section provides details of waste related legislation relevant to the project. In accordance with cradle to grave responsibilities, the Contractor will be responsible for all waste arisings from the time the waste is generated until it reaches its final destination point. This includes its method of treatment/disposal. The Waste Management Acts 1996-201, give effect to the polluter pays principle effectively stating that the waste producer may be liable for any pollution incidents arising from the management of their waste. There is therefore an onus on the Contractor to ensure that all contractors managing waste on their behalf are legally compliant and technically competent and the waste itself is contained, handled, treated and disposed of in accordance with all relevant regulatory requirements.

A brief description of the main waste related regulatory controls relevant to the project is provided hereunder; however, the list is not exhaustive and should be reviewed and amended at regular intervals in accordance with changing legislation:

3.1.1 Waste Management (Landfill Levy) Regulations 2015, S.I. No. 189/2015

There is a landfill levy prescribed under these regulations.

3.1.2 Waste Management (Facility Permit and Registration) (Amendment) Regulations 2015, S.I. No. 198/2015

These regulations describe the process for obtaining a Waster Permit or Certificate of Registration, by a private operator from a local authority, or a Certificate of Registration from the Environmental Protection Agency (EPA) in respect of a local authority run waste activity which requires registration.

3.1.3 Waste Management (Licensing) (Amendment) Regulations 2010, S.I. No. 350/2010

These regulations relate to the process for obtaining a waste licence from the EPA for the operation of certain waste recovery or disposal facilities under Part V of the Waste Management Act.

3.1.4 Waste Management (Collection Permit) (Amendment) Regulations 2016, S.I. No. 24/2016

These regulations relate to the requirement to obtain a waste collection permit from the relevant local authority for the collection of waste on a commercial basis.

3.1.5 Waste Management (Movement of Hazardous Waste) Regulations 1998, S.I. No. 14/1998

These regulations control the movement of hazardous waste within Ireland requiring authorisation in the form of C1 consignment forms. The C1 form is completed by the Consignor, the Carrier and the Consignee. A three part document provides a tracking mechanism for the hazardous waste from its point of origin to its final destination.

3.1.6 Waste Management (Shipments of Waste) Regulations 2007, S.I. No. 419/2007

These regulations control the movement of waste across member states. Shipments are controlled under a TFS (Transfrontier Shipment) form, which designates the waste under the categories of Green, Amber and Red List. Dublin City Council is the designated competent authority under the regulations.

3.1.7 Waste Classification, List of Waste and Determining if Waste is Hazardous or Non-Hazardous, 2015

This document allows the generators of waste to classify the waste as hazardous or non-hazardous and in the process assigning the correct List of Waste entry. The waste classification system applies across the EU and is the basis for all national and international waste reporting obligations. Correct classification is the foundation for ensuring that collection, transportation, storage, treatment of waste is carried out in a manner that provides protection for the environment and human health and in compliance with legal requirements.

3.1.8 Carriage of Dangerous Goods by Road Regulations 2015, S.I. No. 288/2015

These regulations require drivers transporting dangerous goods to be ADR trained. In addition, a Dangerous Goods Safety Advisor (DGSA) must be appointed where activities include the carriage, or related packing, loading, filling or unloading of dangerous goods by road.

4 Preliminary Construction Traffic Management

This section, relating to the Preliminary Construction Traffic Management Plan (CTMP), sets out the traffic management requirements that will apply to Contractors who are engaged in the demolition and construction activities associated with the proposed development located on the Lands known as "RB Central" at Rockbrook, Carmanhall Road, Sandyford Business District, Sandyford, Dublin 18. The Contractor must adopt the requirements of this Construction Traffic Management Plan into his own Construction Traffic Management Plan and must agree same with Dun Laoghaire Rathdown County Council prior to commencement on site.

4.1 Construction Traffic Access to the Site

4.1.1 Location and access to the site

It is anticipated that the Carmanhall Road and Blackthorn Drive will serve as the main arterial routes for construction traffic from the M50 junction. Refer to Figure 2 for illustration. The site currently has pedestrian and vehicular access points from Blackthorn Drive, as well as a pedestrian access from carmanhall Road. The Contractor will ensure that entrance points to the construction zone are controlled as required. Carmanhall Road and Blackthorn Drive are to remain open during the course of the works.

The Main Contractor will be responsible for all site access and works activity and must ensure the continued operation of Carmanhall Road and Blackthorn Drive. It is proposed that construction vehicles will primarily access the site via a new temporary Carmanhall Road construction entrance (see Figure 2).



Figure 2 - Location map of development and site access route

The management of construction traffic on the public road network around the development will be a critical part of the overall project and must be actively managed by the Contractor.

The Contractor must submit a Construction Traffic Management Plan to the Local Authority for approval. Haulage vehicle movements should be fully coordinated to comply with the requirements of the agreed plan:

- Construction vehicles must not stop or park along the routes at any time;
- Haulage vehicles must not travel in convoys greater than two vehicles at any time;
- Site entrance to remain free of parked or stationary vehicles at all times;
- All loading of demolition material will occur within the site boundary;
- All off-loading of deliveries will take place within the site, remote from the public road and will access via the agreed construction access point.

The site is located in an urban area where the road and junction space is shared with public road users and the flow of construction traffic will need to be marshalled and controlled to ensure that potential conflicts are avoided as much as possible.

4.1.2 Definition of Construction Traffic

Construction traffic means the following vehicles:

- HGVs & haul trucks - i.e. vehicle with 6 tyres or more as set out in the RSA publication 'Guidelines on Maximum Weights and Dimensions of Mechanically Propelled Vehicles and Trailers, Including Manoeuvrability Criteria'
- Site machinery such as excavators, tippers, bulldozers, etc.
- Concrete trucks.

Smaller vehicles used by construction workers to access the site, such as cars and vans, are not deemed to be construction traffic.

4.2 Management of Construction Traffic around the Carmanhall Road Site

The Contractor is required to control the construction traffic in and around the proposed development location, with access to the site via Carmanhall Road. The Contractor must adhere to the following:

- Communicate clearly to all construction staff and subcontractors that they are bound by these restrictions.
- Schedule site traffic in advance to ensure that these restrictions are adhered to.
- Monitor construction traffic at key points remote from the site to check compliance.
- Details of the Contractor's management plan must be submitted to Dun Laoghaire Rathdown County Council in advance of construction and included as part of the Construction Management Plan.
- Vehicle movements associated with ancillary, maintenance and other non-essential activities will be minimised during the peak traffic hours on the public road in the vicinity of the site. Please refer to section 2.7.3 above for details regarding proposed working hours.
- A special permit for moving oversized and hazardous loads will be obtained from DLRCC/ An Garda Síochána prior to any such movements.
- Daily construction programmes will be planned to minimise the number of disruptions to surrounding streets by staggering HGV movements to avoid site queues.
- There will be limited site parking, sufficient only to serve those directly involved with the works.

- Construction vehicles will follow the road hierarchy as much as practicable - i.e. construction vehicles will be directed away from local or minor streets and roads and will be required to use designated primary national and regional routes for accessing the site.
- The Contractor will appoint a Traffic Management Coordinator who will be responsible for the coordination of all traffic safety and traffic management matters. The Traffic Management Coordinator will ensure that all traffic management requirements set-out in the CTMP are met.
- In the event that multiple contractors will be working on site, overall traffic management coordination will be required. This will include a review of the individual CTMPs prepared by different Contractors and provision of guidance to ensure consistency between them. An overall CTMP for the entire site should be prepared and agreed with DLRCC in advance of commencement of works.

4.3 Proof of Compliance with Traffic Restrictions

The Contractor will track the transit of construction traffic in the area for the duration of the works.

The Contractor will control traffic movements using the following procedure;

- Develop a restrictions and rule adherence form that all lorry drivers and site operatives will sign.
- All traffic movements to and from site to be managed by the Contractor's transport manager in accordance with these restrictions
- Appointed person located at the site entrance to issue docketts and record all traffic entering and leaving site.
- Records to be reviewed periodically by the site manager.
- Prior to any new contractors starting, all persons must sign up to restrictions and prequalification forms.
- A certified Flagman must be present to coordinate the traffic entering and leaving the site.

4.4 Construction Traffic Access to site via Carmanhall Road

4.4.1 Traffic Management Procedures / Generation

All deliveries will be booked into site at least one day before delivery. All drivers will contact the site gate man 15 minutes before arrival on site.

All construction traffic will arrive along the public road, with entry to the site via the construction site's southern site boundary. All deliveries will be off-loaded without delay by the most appropriate method and escorted off site.

The site gate man will be responsible for ensuring that there is no conflict between pedestrians and vehicles / entering / exiting the site.

It is predicted that there will be between 30-200 personnel on site during peak construction activity. Accounting for car sharing, there could be in the order of 20 vehicles arriving and departing the site every day during peak construction activity.

Please refer to section 2.7.3 and 2.7.8 above for additional information regarding traffic and working hours.

It is expected that there will be only one stage this project that will generate HGV movements; demolition works.

Please refer to section 2.7.8 and 2.7.9 above for outline of information regarding proposed HGV movements.

4.4.2 Traffic management - Internal Site Extents

Site operatives will be encouraged to avail of local public transport to travel to and from the site. Local public transport in the area includes various bus services, as well as the LUAS Green line.

Contractor / subcontractor / supplier parking is not permitted on any illegal locations. Vehicles must be parked within approved designated areas within the site extents or at legal parking locations off site. As outlined in Section 2.7.7 above, there will be limited parking available within the site extents (within the existing basement). To minimise congestion, a traffic management plan will need to be developed by the Contractor to ensure that construction workers access the site using alternative means of transport (i.e. public transport) to negate impacts on the local network and local parking areas.

No unloading or blockages of access routes, including emergency vehicle access routes. Such vehicles will be immediately requested to move to avoid impeding works.

In accordance with this CTMP, the Contractor must appoint a Traffic Management Coordinator responsible for the management of traffic management related activities on site.

The Contractor must carry out an auto-track analysis to ensure that adequate turning space is available. The auto-track must demonstrate how construction vehicles will go in and out of the site. Contractors must eliminate where possible the necessity for reversing of any construction or supply chain vehicle onsite.

The contractor is to note requirement for traffic management, and parking is to be incorporated into the contractors temporary traffic management plan. The contractor's temporary traffic management plan shall be in accordance with Part 8 of the Traffic Signs Manual and DLRCC requirements.

4.4.3 Traffic management coordination meetings

Monthly logistics coordination will be undertaken where the traffic management strategy, traffic management coordination (and implementation of any required temporary traffic management schemes) will be discussed and agreed.

4.4.4 Construction Access Road required behaviours

The Contractor must adhere to established traffic management measures specified in the Construction Traffic Management Plan including:

- Queuing procedures outside the site for vehicles seeking to enter the site to prevent back-up onto the local road network;
- Sign-in requirements;
- Visual PPE checks;
- Arrangements for infrequent visitors, e.g. project team, client visitors;
- Compliance to sign-in requirements, use of turnstiles and/or swipe cards; and
- Collaborate with any required security searches of vehicles entering or exiting.

All Contractors will be deemed to have inspected and examined the site and its surroundings at tender stage and to have satisfied itself as to the nature and means of access to the site.

In the event of a Contractor not being satisfied with the permitted access routes to and from the site, the Contractor is obliged to provide for all expenses and charges for temporary way-leaves and temporary truck/vehicle holding areas in connection with different access arrangements to the site. Any amendments must be to the satisfaction of DLRCC.

4.4.5 Loading/Unloading locations

Vehicles must be loaded and unloaded within the construction works operations site area (i.e. access routes, site compound set-up and loading areas as developed by the Contractor and agreed with the relevant local authority). Contractors are not permitted to carry out loading or unloading on the public roadway without permission from the relevant local authority. This approach reduces the risk to the public, reduces congestion, and minimises disruption and risk to any passing vehicles on the highway. All deliveries and collections should be overseen and managed for the Contractor by a nominated competent person.

Contractors must consider and explain how to manage the impacts on cyclists, pedestrians, other road users, and any affected roadway infrastructure.

4.4.6 Emergency Access

Access for emergency vehicles via the primary haul roads must be maintained at all times.

4.4.7 Asset Protection

The Contractor must take care to avoid damage to roads, footpaths, grass margins, and other surfaces and all walls including protected walls, structures including protected structures and the associated curtilage, trees, lighting fixtures and all other street furniture within or outside of the overall site. They shall be liable for the cost of repairing / replacing all such damage caused by its operations to the satisfaction of DLRCC.

Contractors must take precautions to ensure against spillage of diesel fuel, contaminated water or solvents. Any damage so caused shall be made good by the offending Contractor at its own expense. There may also be repercussions relating to planning conditions for which the Contractor will be liable.

Contractors must prohibit the use of tracked plant on road surfaces outside of the site unless suitably approved protective measures are taken to safeguard the integrity of surfaces.

The Contractors Construction Management Plan must include specifications regarding the quality of temporary reinstatements and the timelines for permanent reinstatements of roads and pavements affected by the works.
